

ID	Task Name	Contract S	Contract F	Mile Stones	% Comp	Plan Start	Plan Finish	Jul '04	Aug '04	Sep '04	Oct '04	Nov '04	Dec '04	Jan '05	Feb '05	Mar '05	Apr '05	May '05	Jun '05	Jul '05	Aug '05	Sep '05	Oct '05	Nov '05	Dec '05	Jan '06	Feb '06								
								27/14	11/18/25/1	8/15/22/29/5	12/19/26/3	10/17/24/31/7	14/21/28/5	12/19/26/2	9/16/23/30/6	13/20/27/6	11/3/20/27/3	10/17/24/1	8/15/22/29/5	12/19/26/3	10/17/24/31/7	14/21/28/4	11/8/25/2	9/16/23/30/6	13/20/27/4	11/8/25/1	8/15/22/29/5	12/19/26/3	10/17/24/31/7	14/21/28/5	11/8/25/2	9/16/23/30/6	13/20/27/4	11/8/25/1	8/15/22/29/5
1	Submit Proposal	Thu 7/22/04	Thu 7/22/04		100		NA	NA	7/22																										
2	Teleconference to discuss Proposal	Mon 7/26/04	Fri 7/30/04		100		NA	NA	7/26																										
3	Receive Order	Fri 9/24/04	Fri 9/24/04		100		NA	NA	9/24																										
4	WO# 65678 PPPL VVSA Lot # 14	Thu 9/2/04	Tue 11/22/05				NA	NA	WO# 65678 PPPL VVSA Lot #																										
5	Start Up/Engineering QLI#1	Fri 9/24/04	Thu 12/30/04						Start Up/Engineering QLI#1																										
6	Process Order	Fri 9/24/04	Thu 12/30/04		70	Thu 12/30/04	Mon 4/18/05		Process Order																										
7	Sect 5.1 Segmentation Scheme	Thu 11/4/04	Fri 11/19/04		75	Thu 11/4/04	Mon 1/17/05		Sect 5.1 Segmentation Scheme																										
8	Sect 5.1.2 Fiducials	Mon 11/29/04	Fri 12/17/04		55	Mon 1/17/05	Fri 2/4/05		Sect 5.1.2 Fiducials																										
9	Sect 5.1.3 Proc Outline & Asc Procedu	Fri 9/24/04	Fri 12/10/04		95	Fri 12/10/04	Fri 3/4/05		Sect 5.1.3 Proc Outline & Asc Procedures																										
10	Special Tooling QLI# 2	Thu 9/2/04	Fri 5/20/05						Special Tooling QLI# 2																										
11	Dies & Gages Lot # 10	Thu 9/2/04	Fri 2/25/05						Dies & Gages Lot # 10																										
12	Engineering	Thu 9/2/04	Wed 12/1/04		100	Wed 12/1/04	Fri 1/28/05		Engineering																										
13	Procure Materials (10 sets was 4)	Mon 11/15/04	Fri 1/7/05		215	Fri 1/7/05	Wed 3/9/05		Procure Materials (10 sets was 4)																										
14	Machine Complete	Wed 12/1/04	Fri 1/28/05		24	Fri 1/28/05	Wed 3/23/05		Machine Complete																										
15	Deburr	Fri 12/10/04	Fri 2/4/05		10	Fri 2/4/05	Mon 3/28/05		Deburr																										
16	Inspection	Fri 12/17/04	Fri 2/11/05		239	Fri 2/11/05	Wed 3/30/05		Inspection																										
17	Development Panels	Mon 12/27/04	Fri 2/25/05			Fri 2/25/05	Fri 4/15/05		Development Panels																										
18	Fixtures (2) 60 degree Lot # 11	Mon 10/25/04	Wed 3/9/05						Fixtures (2) 60 degree Lot # 11																										
19	Engineering	Mon 10/25/04	Fri 12/17/04		98	Fri 12/17/04	Sat 2/26/05		Engineering																										
20	Procure Materials	Fri 12/17/04	Fri 1/14/05			Fri 1/14/05	Sat 3/5/05		Procure Materials																										
21	Fab & Machine Complete	Fri 1/14/05	Thu 2/17/05			Thu 2/17/05	Sun 4/3/05		Fab & Machine Complete																										
22	Assemble	Fri 2/18/05	Thu 2/24/05			Thu 2/24/05	Sat 4/30/05		Assemble																										
23	Deburr	Fri 2/25/05	Thu 3/3/05			Thu 3/3/05	Sat 5/7/05		Deburr																										
24	Inspection	Fri 3/4/05	Wed 3/9/05			Wed 3/9/05	Sat 5/14/05		Inspection																										
25	Fixture (3) 120 degree Lot # 12	Thu 1/6/05	Fri 5/20/05						Fixture (3) 120 degree Lot # 12																										
26	Engineering	Thu 1/6/05	Fri 2/4/05		10	Sun 1/30/05	Fri 4/15/05		Engineering																										
27	Procure Materials	Wed 1/19/05	Fri 2/4/05		220	Sun 3/13/05	Fri 5/13/05		Procure Materials																										
28	Fab & Machine Complete	Mon 2/7/05	Wed 4/27/05			Wed 4/27/05	Thu 6/23/05		Fab & Machine Complete																										
29	Assemble	Thu 4/28/05	Wed 5/4/05			Wed 5/4/05	Sun 7/24/05		Assemble																										
30	Deburr	Thu 5/5/05	Thu 5/12/05			Thu 5/12/05	Sun 8/7/05		Deburr																										
31	Inspection	Fri 5/13/05	Fri 5/20/05			Mon 7/4/05	Thu 7/14/05		Inspection																										
32	Procure Vessel Material	Fri 10/29/04	Fri 2/25/05		290	Fri 2/25/05	Mon 3/21/05		Procure Vessel Material																										
33	Production Panels Period #1 Lot # 4	Fri 2/25/05	Tue 4/26/05		260	Tue 4/26/05	Mon 5/2/05		Production Panels Period #1 Lot # 4																										
34	Production Panels Period #2 Lot # 5	Fri 4/22/05	Fri 6/3/05		200	Fri 6/3/05	Fri 6/10/05		Production Panels Period #2 Lot # 5																										
35	Production Panels Period #3 Lot # 6	Tue 5/17/05	Tue 6/28/05		200	Tue 6/28/05	Tue 7/5/05		Production Panels Period #3 Lot # 6																										
36	Port Ext.Misc Hardware Period #1 Lot # 7	Mon 4/11/05	Tue 7/5/05			Tue 7/5/05	Tue 7/12/05		Port Ext.Misc Hardware Period #1 Lot # 7																										
37	Port Ext.Misc Hardware Period # 2 Lot # 8	Mon 5/30/05	Tue 8/9/05			Tue 8/9/05	Tue 8/16/05		Port Ext.Misc Hardware Period # 2 Lot # 8																										


Summary Contract Milestone Planned Completed



NCSX VVSA for PPPL
Subcontract S005243-F
MTM WO# 65678



ID	Task Name	Contract S	Contract F	Mile Stones	% Comp	Plan Start	Plan Finish	Jul '04	Aug '04	Sep '04	Oct '04	Nov '04	Dec '04	Jan '05	Feb '05	Mar '05	Apr '05	May '05	Jun '05	Jul '05	Aug '05	Sep '05	Oct '05	Nov '05	Dec '05	Jan '06	Feb '06
38	Port Ext. Misc Hardware Period #4 Lot # 9	Mon 6/27/05	Tue 9/6/05			Tue 9/6/05	Tue 9/13/05																				
39	(1) Spacer (3) Port Ext. Fixtures Lot # 13	Thu 2/17/05	Fri 6/3/05			Fri 6/3/05	Sun 9/18/05																				
40	First 120 deg seg QLI #3 Lot # 1	Tue 3/29/05	Wed 10/19/05																								
41	1st 60 deg segment	Tue 3/29/05	Tue 5/10/05			Tue 5/10/05	Sun 5/29/05																				
42	2nd 60 deg segment	Tue 5/3/05	Fri 6/3/05			Fri 6/3/05	Sun 6/19/05																				
43	Join two pieces	Sun 5/22/05	Tue 6/14/05	350		Tue 6/14/05	Tue 7/5/05																				
44	Machine for Ports	Tue 6/14/05	Tue 7/5/05			Tue 7/5/05	Sun 7/24/05																				
45	Weld Ports	Tue 7/5/05	Tue 8/16/05			Tue 8/16/05	Sat 9/17/05																				
46	Final Machine	Tue 8/16/05	Tue 9/6/05			Sun 9/18/05	Thu 10/6/05																				
47	Vacuum Test	Tue 9/6/05	Tue 9/20/05			Thu 10/6/05	Thu 10/20/05																				
48	Cut Off Ports	Tue 9/20/05	Tue 10/11/05			Thu 10/20/05	Sun 10/30/05																				
49	Pack for Shipping #1	Tue 10/11/05	Fri 10/14/05			Mon 10/31/05	Wed 11/2/05																				
50	Receive at PPPL	Fri 10/14/05	Wed 10/19/05	375.56		Wed 11/2/05	Mon 11/7/05																				
51	Second 120 deg seg QLI# 3 Lot # 2	Fri 6/3/05	Mon 10/31/05																								
52	60 deg segment	Fri 6/3/05	Fri 7/1/05			Wed 8/3/05	Mon 9/5/05																				
53	60 deg segment	Tue 6/14/05	Tue 7/12/05			Mon 8/15/05	Wed 9/14/05																				
54	Join two pieces	Tue 7/5/05	Tue 7/19/05	350		Mon 9/5/05	Mon 9/19/05																				
55	Machine for Ports	Tue 7/19/05	Tue 8/9/05			Mon 9/19/05	Mon 10/10/05																				
56	Weld Ports	Tue 8/9/05	Tue 9/6/05			Mon 10/10/05	Mon 11/7/05																				
57	Final Machine	Tue 9/6/05	Tue 9/27/05			Mon 11/7/05	Mon 11/28/05																				
58	Vacuum Test	Tue 9/27/05	Tue 10/11/05			Mon 11/28/05	Mon 12/12/05																				
59	Cut Off Ports	Fri 10/7/05	Fri 10/21/05			Mon 12/12/05	Wed 12/21/05																				
60	Pack for Shipping #2	Fri 10/21/05	Thu 10/27/05			Tue 12/27/05	Fri 12/30/05																				
61	Receive at PPPL	Thu 10/27/05	Mon 10/31/05	375		Tue 1/3/06	Thu 1/5/06																				
62	Third 120 deg seg QLI# 3 Lot # 3	Fri 7/1/05	Tue 11/22/05																								
63	60 deg segment	Fri 7/1/05	Fri 7/29/05			Mon 9/19/05	Fri 10/14/05																				
64	60 deg segment	Sun 7/17/05	Fri 8/12/05			Mon 9/26/05	Sun 10/30/05																				
65	Join two pieces	Tue 8/9/05	Tue 8/23/05	375		Mon 10/24/05	Mon 11/7/05																				
66	Machine for Ports	Tue 8/23/05	Tue 9/6/05			Mon 11/7/05	Mon 11/21/05																				
67	Weld Ports	Tue 9/6/05	Tue 9/27/05			Mon 11/21/05	Mon 12/12/05																				
68	Final Machine	Tue 9/27/05	Tue 10/11/05			Mon 12/12/05	Thu 12/22/05																				
69	Vacuum Test	Tue 10/11/05	Tue 10/25/05			Tue 12/27/05	Mon 1/16/06																				
70	Cut Off Ports	Tue 10/25/05	Tue 11/15/05			Mon 1/16/06	Wed 2/15/06																				
71	Pack for Shipping #3	Tue 11/15/05	Fri 11/18/05			Wed 2/15/06	Fri 2/17/06																				
72	Receive at PPPL	Fri 11/18/05	Tue 11/22/05	375		Fri 2/17/06	Fri 2/24/06																				
73	Pack for PPPL Tooling	Fri 11/18/05	Fri 11/25/05	432		Fri 2/17/06	Fri 2/24/06																				
74	Receive at PPPL Tooling	Mon 11/28/05	Thu 12/1/05	486		Mon 2/27/06	Thu 3/2/06																				

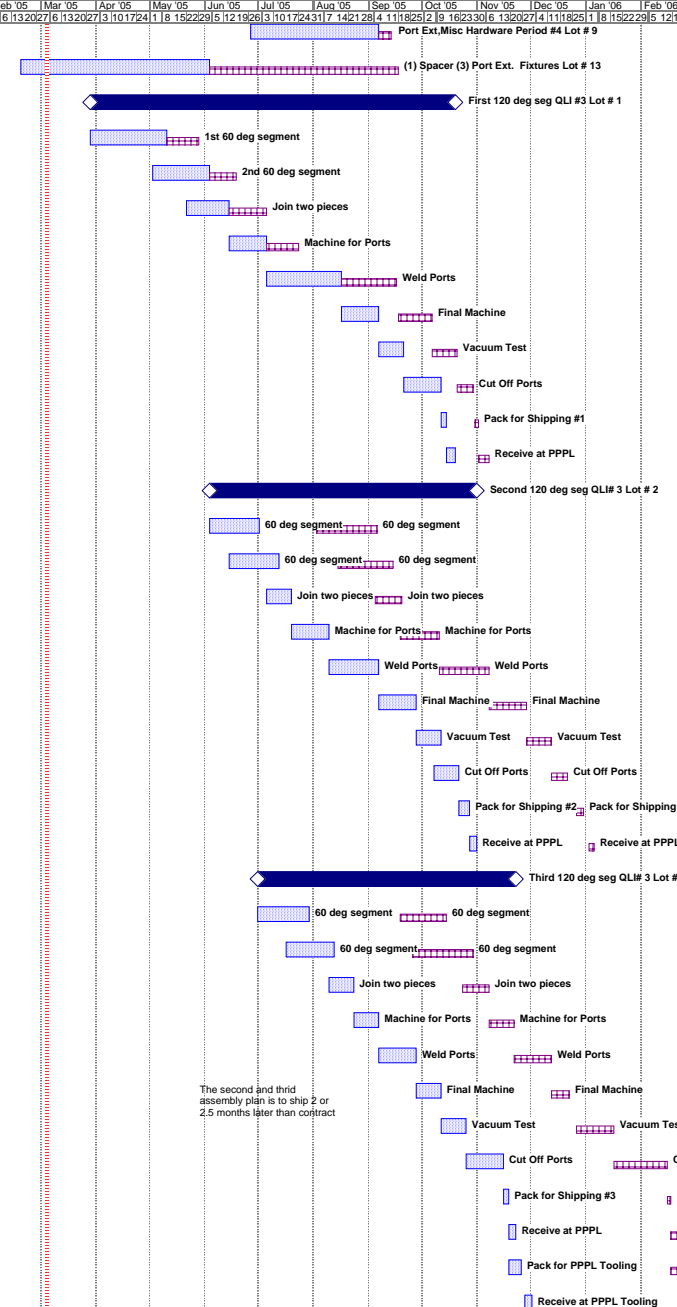

Summary Contract Milestone Planned Completed
