


ID	Task Name	Contract S	Contract F	Mile Stones	% Comp	Jul '04	Aug '04	Sep '04	Oct '04	Nov '04	Dec '04	Jan '05	Feb '05	Mar '05	Apr '05	May '05	Jun '05	Jul '05	Aug '05	Sep '05	Oct '05	Nov '05	Dec '05	Jan '06	Feb '06
1	Submit Proposal	7/22/04	7/22/04		100	7/22																			
2	Teleconference to discuss Proposal	7/26/04	7/30/04		100																				
3	Receive Order	9/24/04	9/24/04		100																				
4	WO# 65678 PPPL VVSA Lot # 14	9/2/04	11/22/05																						
5	Start Up/Engineering QLI#1	9/24/04	12/30/04																						
6	Process Order	9/24/04	12/30/04		70																				
7	Sect 5.1 Segmentation Scheme	11/4/04	11/19/04		75																				
8	Sect 5.1.2 Fiducials	11/29/04	12/17/04		55																				
9	Sect 5.1.3 Proc Outline & Asc Procedu	9/24/04	12/10/04		95																				
10	Special Tooling QLI# 2	9/2/04	5/20/05																						
11	Dies & Gages Lot # 10	9/2/04	2/25/05																						
12	Engineering	9/2/04	12/1/04		100																				
13	Procure Materials (10 sets was 4)	11/15/04	1/7/05		215																				
14	Machine Complete	12/1/04	1/28/05		24																				
15	Deburr	12/10/04	2/4/05		10																				
16	Inspection	12/17/04	2/11/05		239																				
17	Development Panels	12/27/04	2/25/05																						
18	Fixtures (2) 60 degree Lot # 11	10/25/04	3/9/05																						
19	Engineering	10/25/04	12/17/04		98																				
20	Procure Materials	12/17/04	1/14/05																						
21	Fab & Machine Complete	1/14/05	2/17/05																						
22	Assemble	2/18/05	2/24/05																						
23	Deburr	2/25/05	3/3/05																						
24	Inspection	3/4/05	3/9/05																						
25	Fixture (3) 120 degree Lot # 12	1/6/05	5/20/05																						
26	Engineering	1/6/05	2/4/05		10																				
27	Procure Materials	1/19/05	2/4/05		220																				
28	Fab & Machine Complete	2/7/05	4/27/05																						
29	Assemble	4/28/05	5/4/05																						
30	Deburr	5/5/05	5/12/05																						
31	Inspection	5/13/05	5/20/05																						
32	Procure Vessel Material	10/29/04	2/25/05		290																				
33	Production Panels Period #1 Lot # 4	2/25/05	4/26/05		260																				
34	Production Panels Period #2 Lot # 5	4/22/05	6/3/05		200																				
35	Production Panels Period #3 Lot # 6	5/17/05	6/28/05		200																				
36	Port Ext,Misc Hardware Period #1 Lot # 7	4/11/05	7/5/05																						
37	Port Ext,Misc Hardware Period # 2 Lot # 8	5/30/05	8/9/05																						

Summary Contract Milestone Planned Completed

ID	Task Name	Contract S	Contract F	Mile Stones	% Comp	Jul '04	Aug '04	Sep '04	Oct '04	Nov '04	Dec '04	Jan '05	Feb '05	Mar '05	Apr '05	May '05	Jun '05	Jul '05	Aug '05	Sep '05	Oct '05	Nov '05	Dec '05	Jan '06	Feb '06
38	Port Ext, Misc Hardware Period #4 Lot # 9	6/27/05	9/6/05			27	4	11	18	25	1	8	15	22	29	5	12	19	26	3	10	17	24	31	7
39	(1) Spacer (3) Port Ext. Fixtures Lot # 13	2/17/05	6/3/05																						
40	First 120 deg seg QLI #3 Lot # 1	3/29/05	10/19/05																						
41	1st 60 deg segment	3/29/05	5/10/05																						
42	2nd 60 deg segment	5/3/05	6/3/05																						
43	Join two pieces	5/22/05	6/14/05	350																					
44	Machine for Ports	6/14/05	7/5/05																						
45	Weld Ports	7/5/05	8/16/05																						
46	Final Machine	8/16/05	9/6/05																						
47	Vacuum Test	9/6/05	9/20/05																						
48	Cut Off Ports	9/20/05	10/11/05																						
49	Pack for Shipping #1	10/11/05	10/14/05																						
50	Receive at PPPL	10/14/05	10/19/05	375.56																					
51	Second 120 deg seg QLI# 3 Lot # 2	6/3/05	10/31/05																						
52	60 deg segment	6/3/05	7/1/05																						
53	60 deg segment	6/14/05	7/12/05																						
54	Join two pieces	7/5/05	7/19/05	350																					
55	Machine for Ports	7/19/05	8/9/05																						
56	Weld Ports	8/9/05	9/6/05																						
57	Final Machine	9/6/05	9/27/05																						
58	Vacuum Test	9/27/05	10/11/05																						
59	Cut Off Ports	10/7/05	10/21/05																						
60	Pack for Shipping #2	10/21/05	10/27/05																						
61	Receive at PPPL	10/27/05	10/31/05	375																					
62	Third 120 deg seg QLI# 3 Lot # 3	7/1/05	11/22/05																						
63	60 deg segment	7/1/05	7/29/05																						
64	60 deg segment	7/17/05	8/12/05																						
65	Join two pieces	8/9/05	8/23/05	375																					
66	Machine for Ports	8/23/05	9/6/05																						
67	Weld Ports	9/6/05	9/27/05																						
68	Final Machine	9/27/05	10/11/05																						
69	Vacuum Test	10/11/05	10/25/05																						
70	Cut Off Ports	10/25/05	11/15/05																						
71	Pack for Shipping #3	11/15/05	11/18/05																						
72	Receive at PPPL	11/18/05	11/22/05	375																					
73	Pack for PPPL Tooling	11/18/05	11/25/05																						
74	Receive at PPPL Tooling	11/28/05	12/1/05	486																					

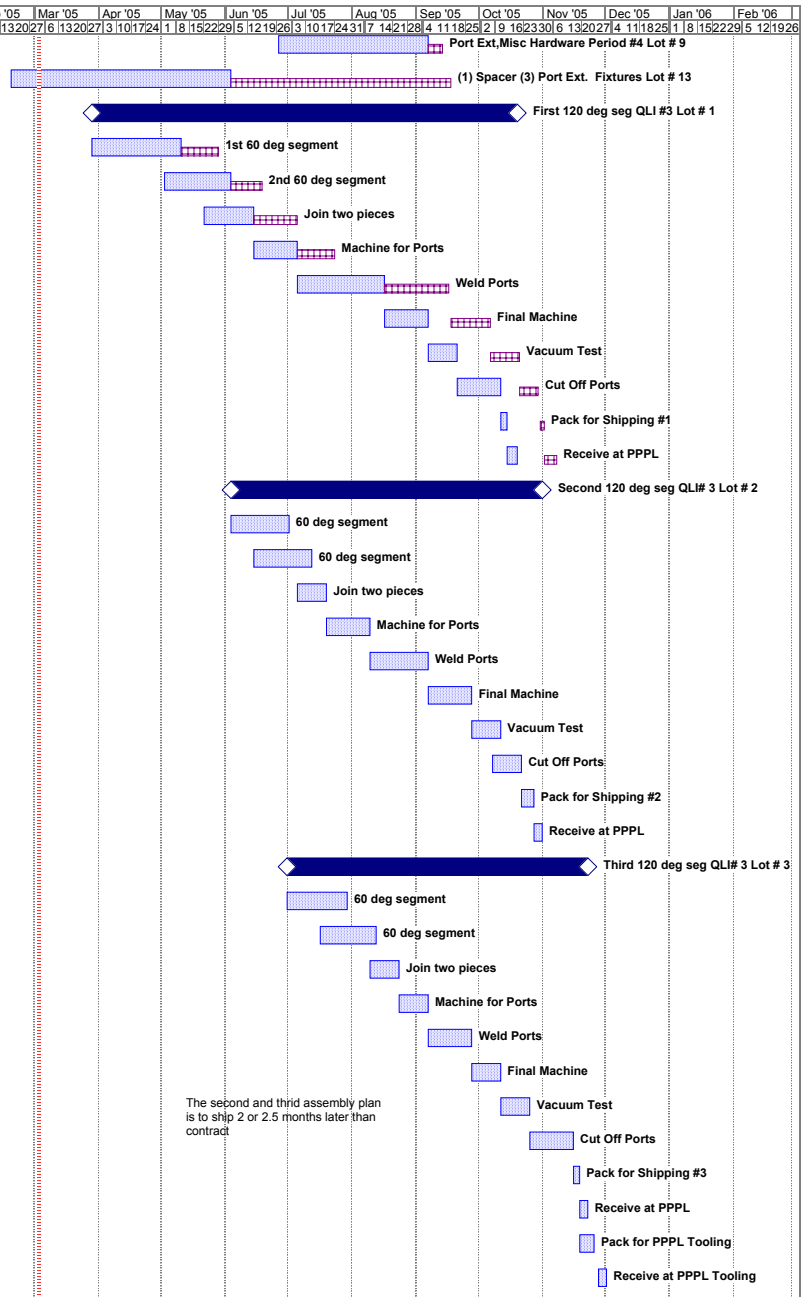

Summary Contract Milestone Planned Completed
