

## Bob Simmons

---

**From:** Ronald L. Strykowski  
**Sent:** Wednesday, October 01, 2008 7:35 AM  
**To:** James H. Chrzanowski; 'Cole, Michael'; 'Jeffrey Harris'; Jeff Harris; Phil Heitzenroeder; Bob Simmons; Michael R. Kalish; Hutch Neilson; Erik D. Perry; Don Rej; Michael E. Viola; Lawrence E. Dudek; Bob Simmons  
**Cc:** Pamela Hampton  
**Subject:** RE: NCSX WEEKLY MEETING-MANDATORY  
**Attachments:** Job8221 sept302008 status.pdf



Job8221  
sept302008 status.pdf

Closeout documentation status for this afternoon's meeting showing only incomplete input.  
Ron

-----Original Message-----

**From:** Ronald L. Strykowski  
**Sent:** Monday, September 29, 2008 1:04 PM  
**To:** James H. Chrzanowski; 'Cole, Michael'; 'Jeffrey Harris'; Jeff Harris; Phil Heitzenroeder; Bob Simmons; Michael R. Kalish; Hutch Neilson; Erik D. Perry; Don Rej; Michael E. Viola; Lawrence E. Dudek  
**Cc:** Pamela Hampton  
**Subject:** NCSX WEEKLY MEETING-MANDATORY

This is at our normal time of 1:00 pm Wednesday in the engr conference room.  
Thanks, Ron

Folks,  
At this Wednesday's meeting we need to do our month close earned value assessment and ETC update. Please come prepared to provide your estimate of FY09 cost for your remaining job scope.  
Attached you'll find any updated copy of the activity barcharts showing only remaining scope. I'll also be sending out a detailed update of the closeout documentation log shortly.

The following folks should come prepared with answers to the following;

JIM CHRZANOWSKI - ETC & schedule for the remaining punch list tasks incl etc for Langish's time

MIKE KALISH - Trim coil drawings signoff  
- Plan for closing out the Everson contract

MIKE COLE - Remaining work scope, if any?

JEFF HARRIS - FY09 plans and ETC against your management job 8102?

PHIL HEITZENROEDER - FY09 plans and ETC against your management job 8202?

DON REJ - Data archiving plans (scope/charge, who, when)? Expected impact to ETC?

BOB SIMMONS - Detailed status for job 8221 (closeout documentation by individual) including last minute ETC updates  
- Issues requiring action on the closeout documentation

HUTCH - Plans for final risk registry update

STRYKOWSKY - FY09 Allocations ETC

VIOLA - Close job 1810?

- HP support to continue against job 1802? (Expectations to the HP folks.)
- FY09 LOE work to continue i.e.; crane/rigging inspections NEED ETC (charge Erik's job 8220?)
- FPA WAF update

IF YOU CANNOT ATTEND PLEASE E-MAIL ME YOUR STATUS AND ETC!

PPPL Participants will meet in the Engineering Conference Room  
Off-site attendees:

Call in number:

866-830-3841

Passcode: 6848450#

# Q: What do you see?



# A: Team Conducting a Critical Operation



# A: Team Conducting a Critical Operation



# A: Team Conducting a Critical Operation




# A: Team Conducting a Critical Operation



# A: Team Conducting a Critical Operation






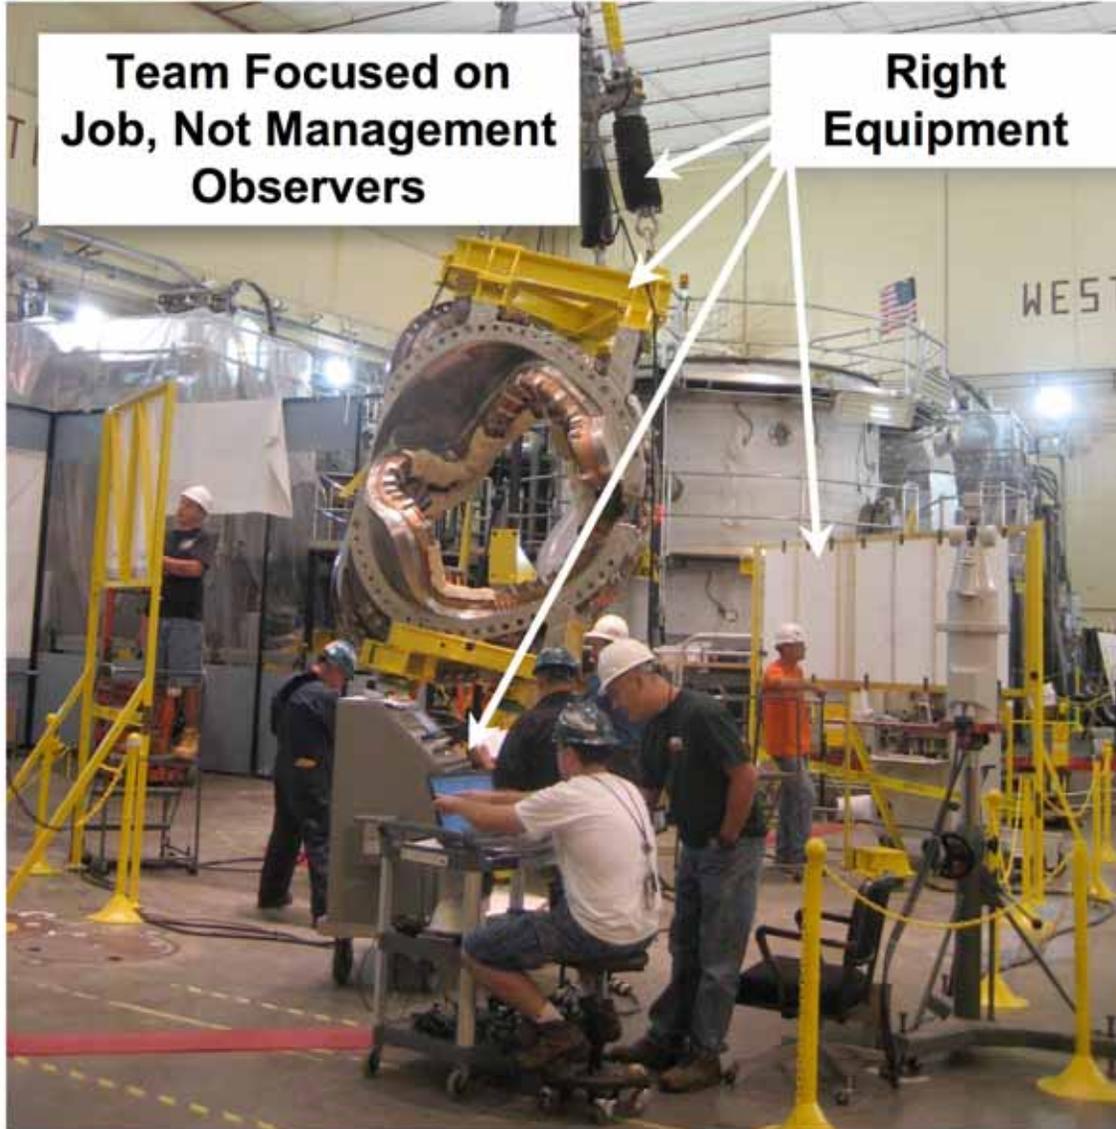

**Team Focused on  
Job, Not Management  
Observers**


**Right  
Equipment**

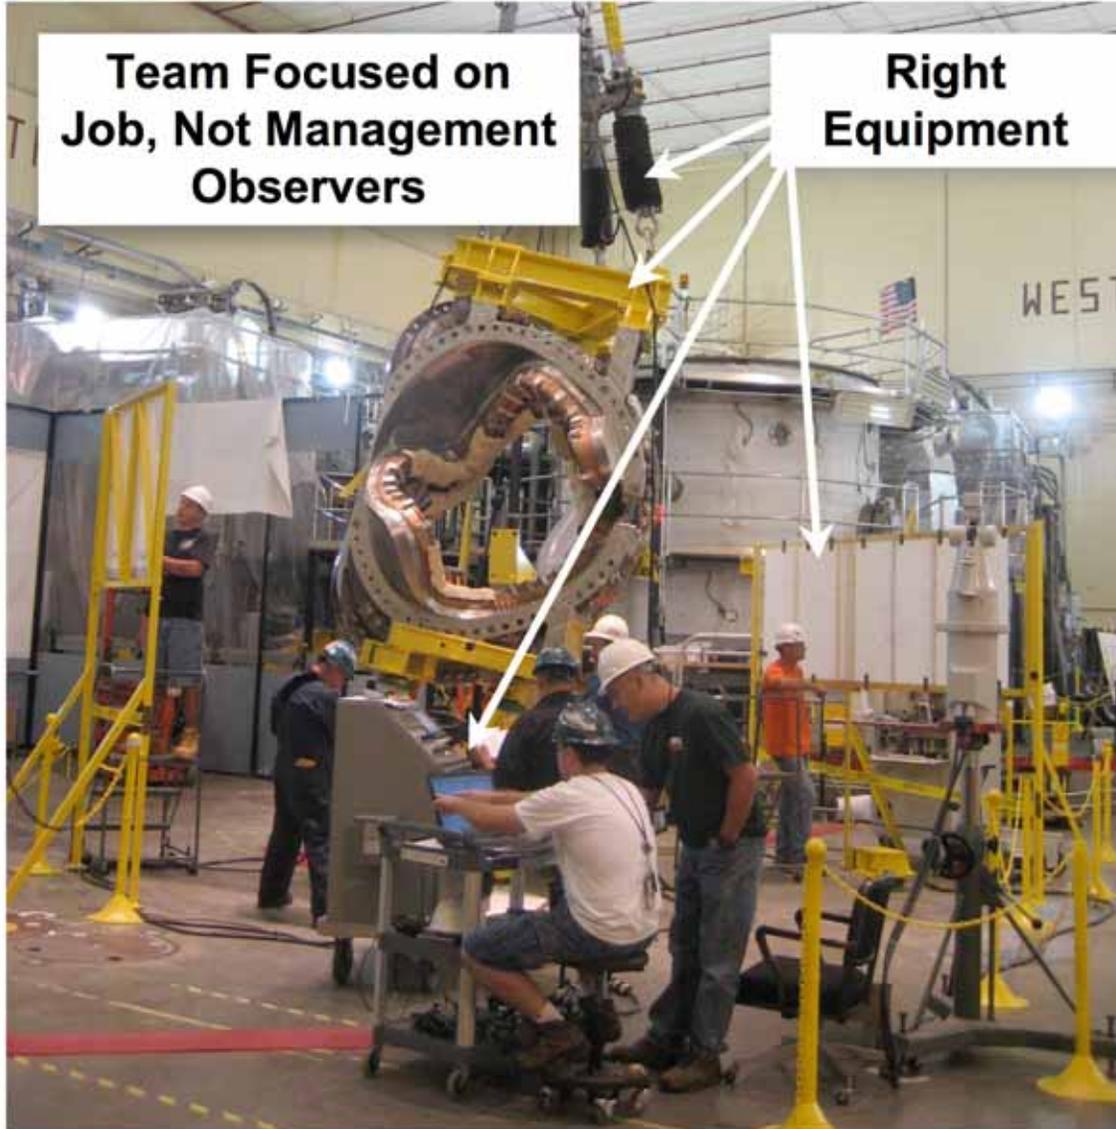

**Team Focused on Job, Not Management Observers**


**Right Equipment**

- Activity:
  - Dry run for NCSX Half-Field Period Assembly to vacuum vessel fit up.

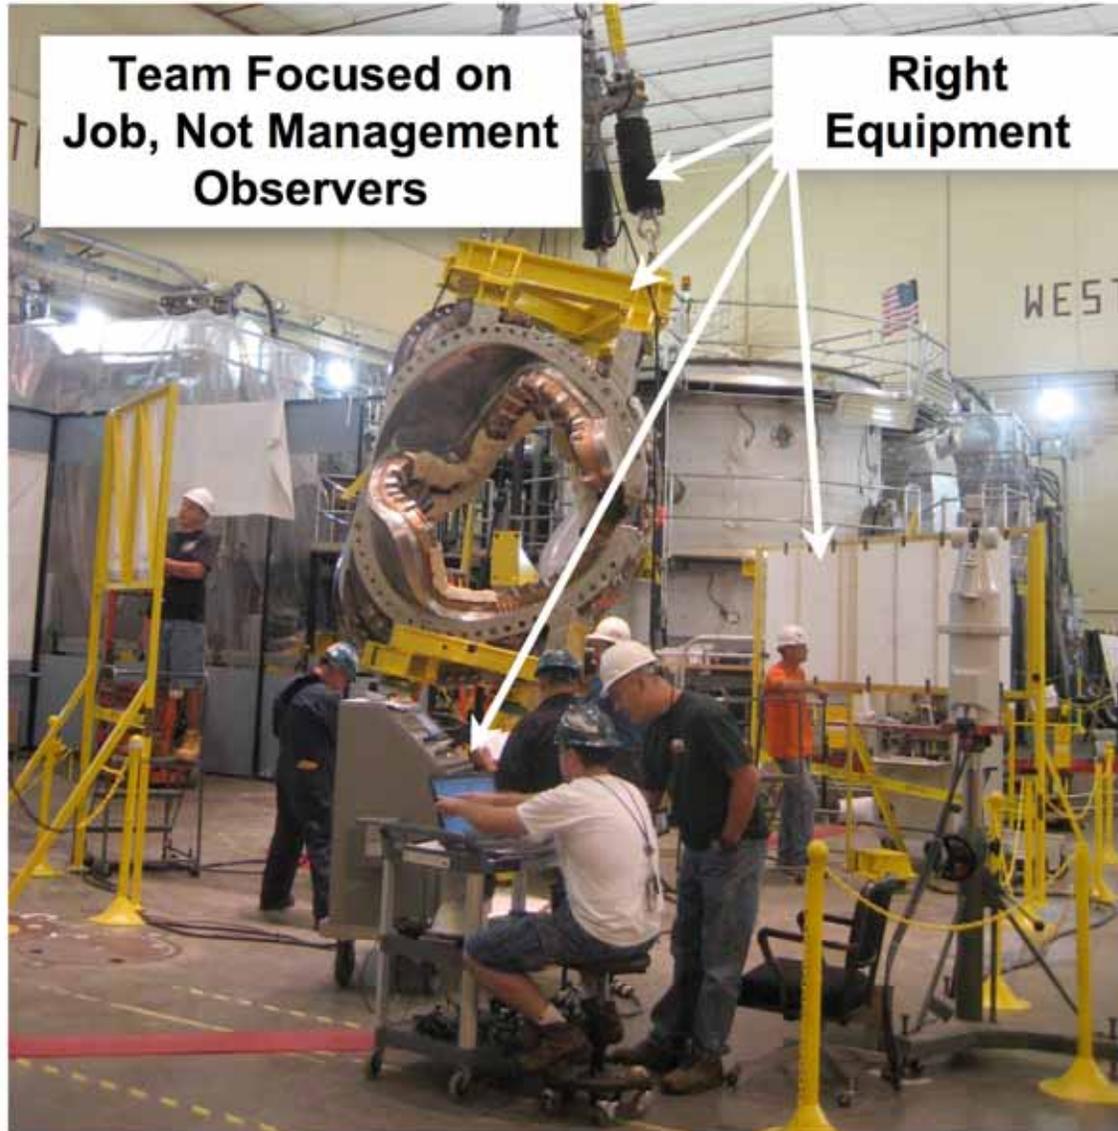

- Activity:
  - Dry run for NCSX Half-Field Period Assembly to vacuum vessel fit up.
- Crew:
  - Capable
  - Communicating
  - Know their job
    - Procedures
    - Interactive & inclusive pre-job brief
  - Trained, equipped, & positioned
  - Promoting an orderly environment

# Team Safety Has Extra Dimensions

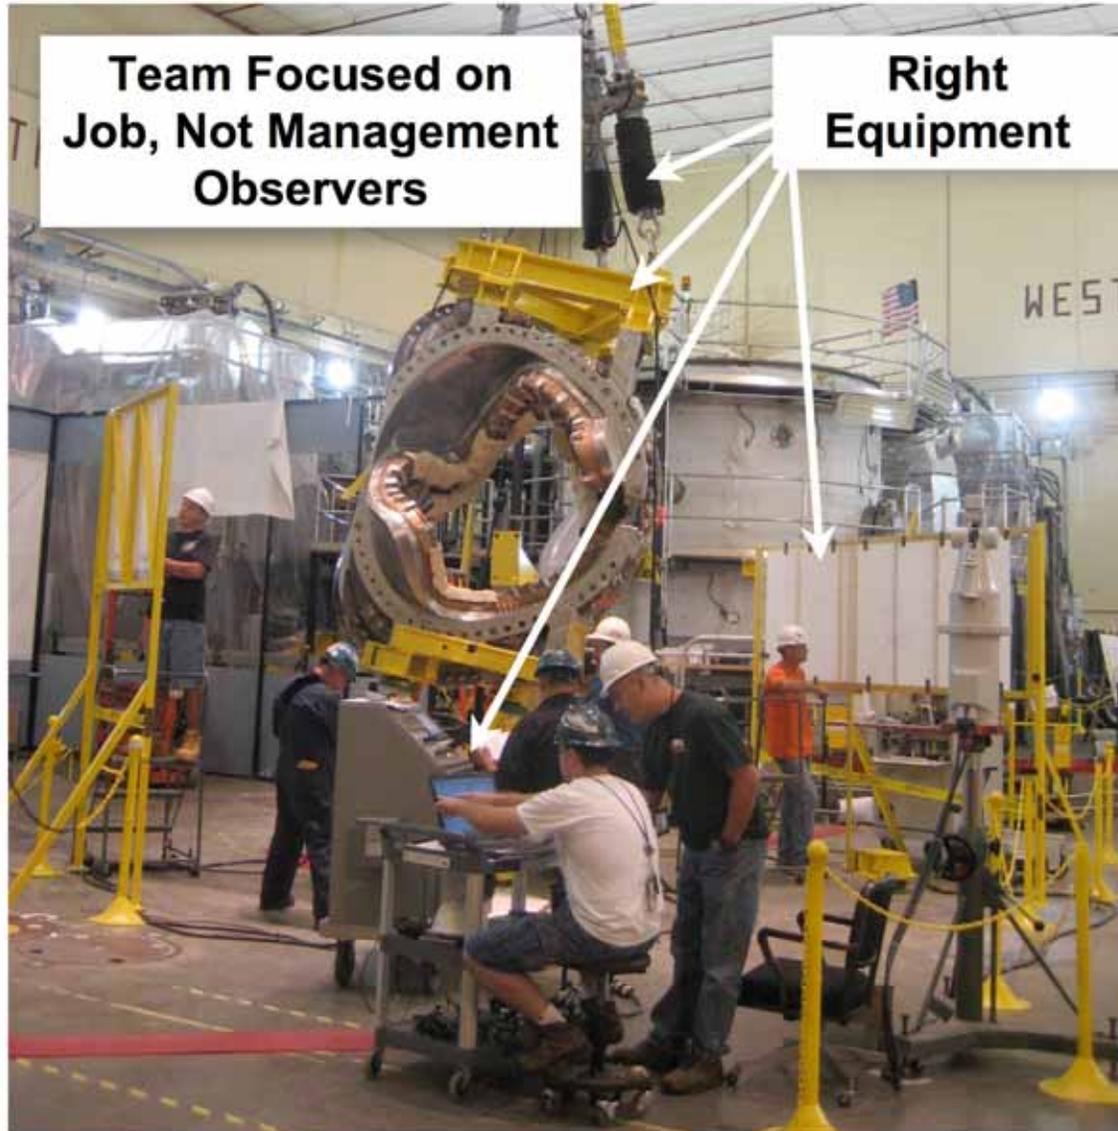

- Activity:
  - Dry run for NCSX Half-Field Period Assembly to vacuum vessel fit up.
- Crew:
  - Capable
  - Communicating
  - Know their job
    - Procedures
    - Interactive & inclusive pre-job brief
  - Trained, equipped, & positioned
  - Promoting an orderly environment

## NCSX Documentation Close-Out Job 8221

STATUS 9/30/08					<del>Estimate to Complete (ETC)</del> Close-Out Notes/Backup Analysis Files (Due Dates)							
Org	Participant		TOTALS (Thru Aug)	ETC	Jobs					Comments		
PPPL	<b>BROOKS</b>	Planned	99		8204					Close out note & backup ANSYS files/models		
		Actual	0	120	9/30							
PPPL	BROWN	Planned	376		1830	8203				Draft received - minor editorial comments needed		
		Actual	0	272	10/15	10/15						
PPPL	<b>DAHLGREN</b>	Planned	560		1353	1501	1702			Close out note & backup ANSYS files/models		
		Actual	160	300	8/29	8/29	8/29			Need new dates & ETC		
PPPL	DODSON	Planned	41		8221					Include hours for as-built drawings		
		Actual	0		10/31							
PPPL	<b>ELLIS</b>	Planned	41		8205					Close out note & backup ANSYS files/models		
		Actual	0		10/2							
PPPL	HEITZENROED	Planned	160		8221							
		Actual	26	80	12/31							
PPPL	KALISH	Planned	57		1361	1354	6401					
		Actual	8	49	10/15	10/15	10/15					
PPPL	LABIK	Planned	41		3101							
		Actual	0	40	10/15							
PPPL	<b>LANGISH</b>	Planned	24		1459							
		Actual	0	70	9/30							
PPPL	MORRIS	Planned	336		1354	1803	1810	8221			Include hours for as-built drawings	
		Actual	40	80	10/15	10/15	11/15	10/31				
PPPL	<b>PERRY</b>	Planned	16		7301	7401	7501	7503	7601	8215	8220	
		Actual	0	16	9/24	9/24	9/24	9/24	9/24	9/24	12/31	
PPPL	<b>PRINISKI</b>	Planned	16		8205					Need backup data files		
		Actual	0		9/30							
PPPL	RAKI	Planned	160		4101	4301	4401	4501			Include designer hours to complete drawings	
		Actual	39		10/3	10/3	10/3	10/3				
PPPL	REIERSEN	Planned	160		8221					Include hours to review overall close out report		
		Actual	0	24	11/30							
PPPL	SIMMONS	Planned	762		8221							
		Actual	304	500	12/31							
PPPL	<b>SMITH</b>	Planned	16		8205							
		Actual	0		9/30							
PPPL	STRATTON	Planned	41		3101	3601	3801	3901				
		Actual	0	10	10/15	10/15	10/15	10/15				
PPPL	STRYKOWSKY	Planned	160		8221							
		Actual	0	360	12/31							
PPPL	VIOLA	Planned	158		1802	1810	1815			Include hours to update FPA assembly estimate		
		Actual	0		11/15	11/15	11/15					
PPPL	<b>ZHANG</b>	Planned	160		8204					Only backup ANSYS files/models needed		
		Actual	0	80	9/30							

