





Activity ID	Activity Description	Orig Dur	Forecast Start	Forecast Finish	Total Float	FY03					FY04										FY05													
						A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	U
Job: 1203 - Vacuum Vessel Final Dsn-GORANSON																																		
121-001	Final Design	135	13OCT03*	29APR04	43																													
121-6-5	VV FDR	0		29APR04	43																													
121-6-5J	JOULE MILESTONE #3-Mod Coil and Vac Vsl FDR	0		29APR04	43																													
121-6-6	Finalize tech Doc package & Resolve chits	15	30APR04	20MAY04	92																													
121-6-8	Evaluate and Select VV Production Vendor	10	21JUN04	02JUL04	170																													
121-6-83	Negotiate with vendor	10	06JUL04	19JUL04	170																													
121-6-85	DOE Approve VV Selection & contract	10	20JUL04	02AUG04	170																													
121-6-9	Award VV Production Vendor (Phase funded)	0		02AUG04	170																													
121-36-9.2	Release for Fabrication	0		02AUG04	170																													
124-001	Title I design WBS 124 VV supports	30	01OCT03*	11NOV03	520																													
124-011	Title II design WBS 124 VV supports	65	01MAR05*	31MAY05	191																													
Job: 1204 - VV Insul, H/C Prel Dsn-GORANSON																																		
122-001	Title I design WBS 122 Thermal insulation	86	01OCT03*	02FEB04	389																													
123-001	Title I design WBS 123 Htg/Cooling	40	01OCT03*	25NOV03	482																													
Job: 1250 - Vacuum Vessel Fabrication-GORANSON																																		
121-031	Title III engr	650	30APR04	16NOV06	1,522																													
121-038	VV vendor fabricate 3 periods (c/1)	303	03AUG04	10OCT05	175																													
121-038P	VV vendor fab, test & deliver ports (c/1)	303	03AUG04	10OCT05	299																													
Job: 1301 - Conventional Coils Prel Design-VIOLA																																		
Project VV/MCC Prelim Design Rww																																		
1301-029	Prelim Vendor Search	42*	01JUL03A	28AUG03	27																													
1301-007	Update Cost and Schedule	59*	23MAY03A	15AUG03	36																													
1301-013	Write approve SEMl	59*	23MAY03A	15AUG03	36																													
1301-016	Prelim Design Report	74*	02JUN03A	15SEP03	16																													
1301-023	Update interfaces for cryostat and coil leads	59*	23JUN03A	15SEP03	16																													
1301-015	Draft Design to Spec	85*	02JUN03A	30SEP03	5																													
Conventional Coils Preliminary Design																																		
1301-017	FEA, Model Global Forces	101*	09JUL03A	01DEC03	92																													
1301-021	Write Prelim Purchase Spec	28*	09JUL03A	15AUG03	156																													

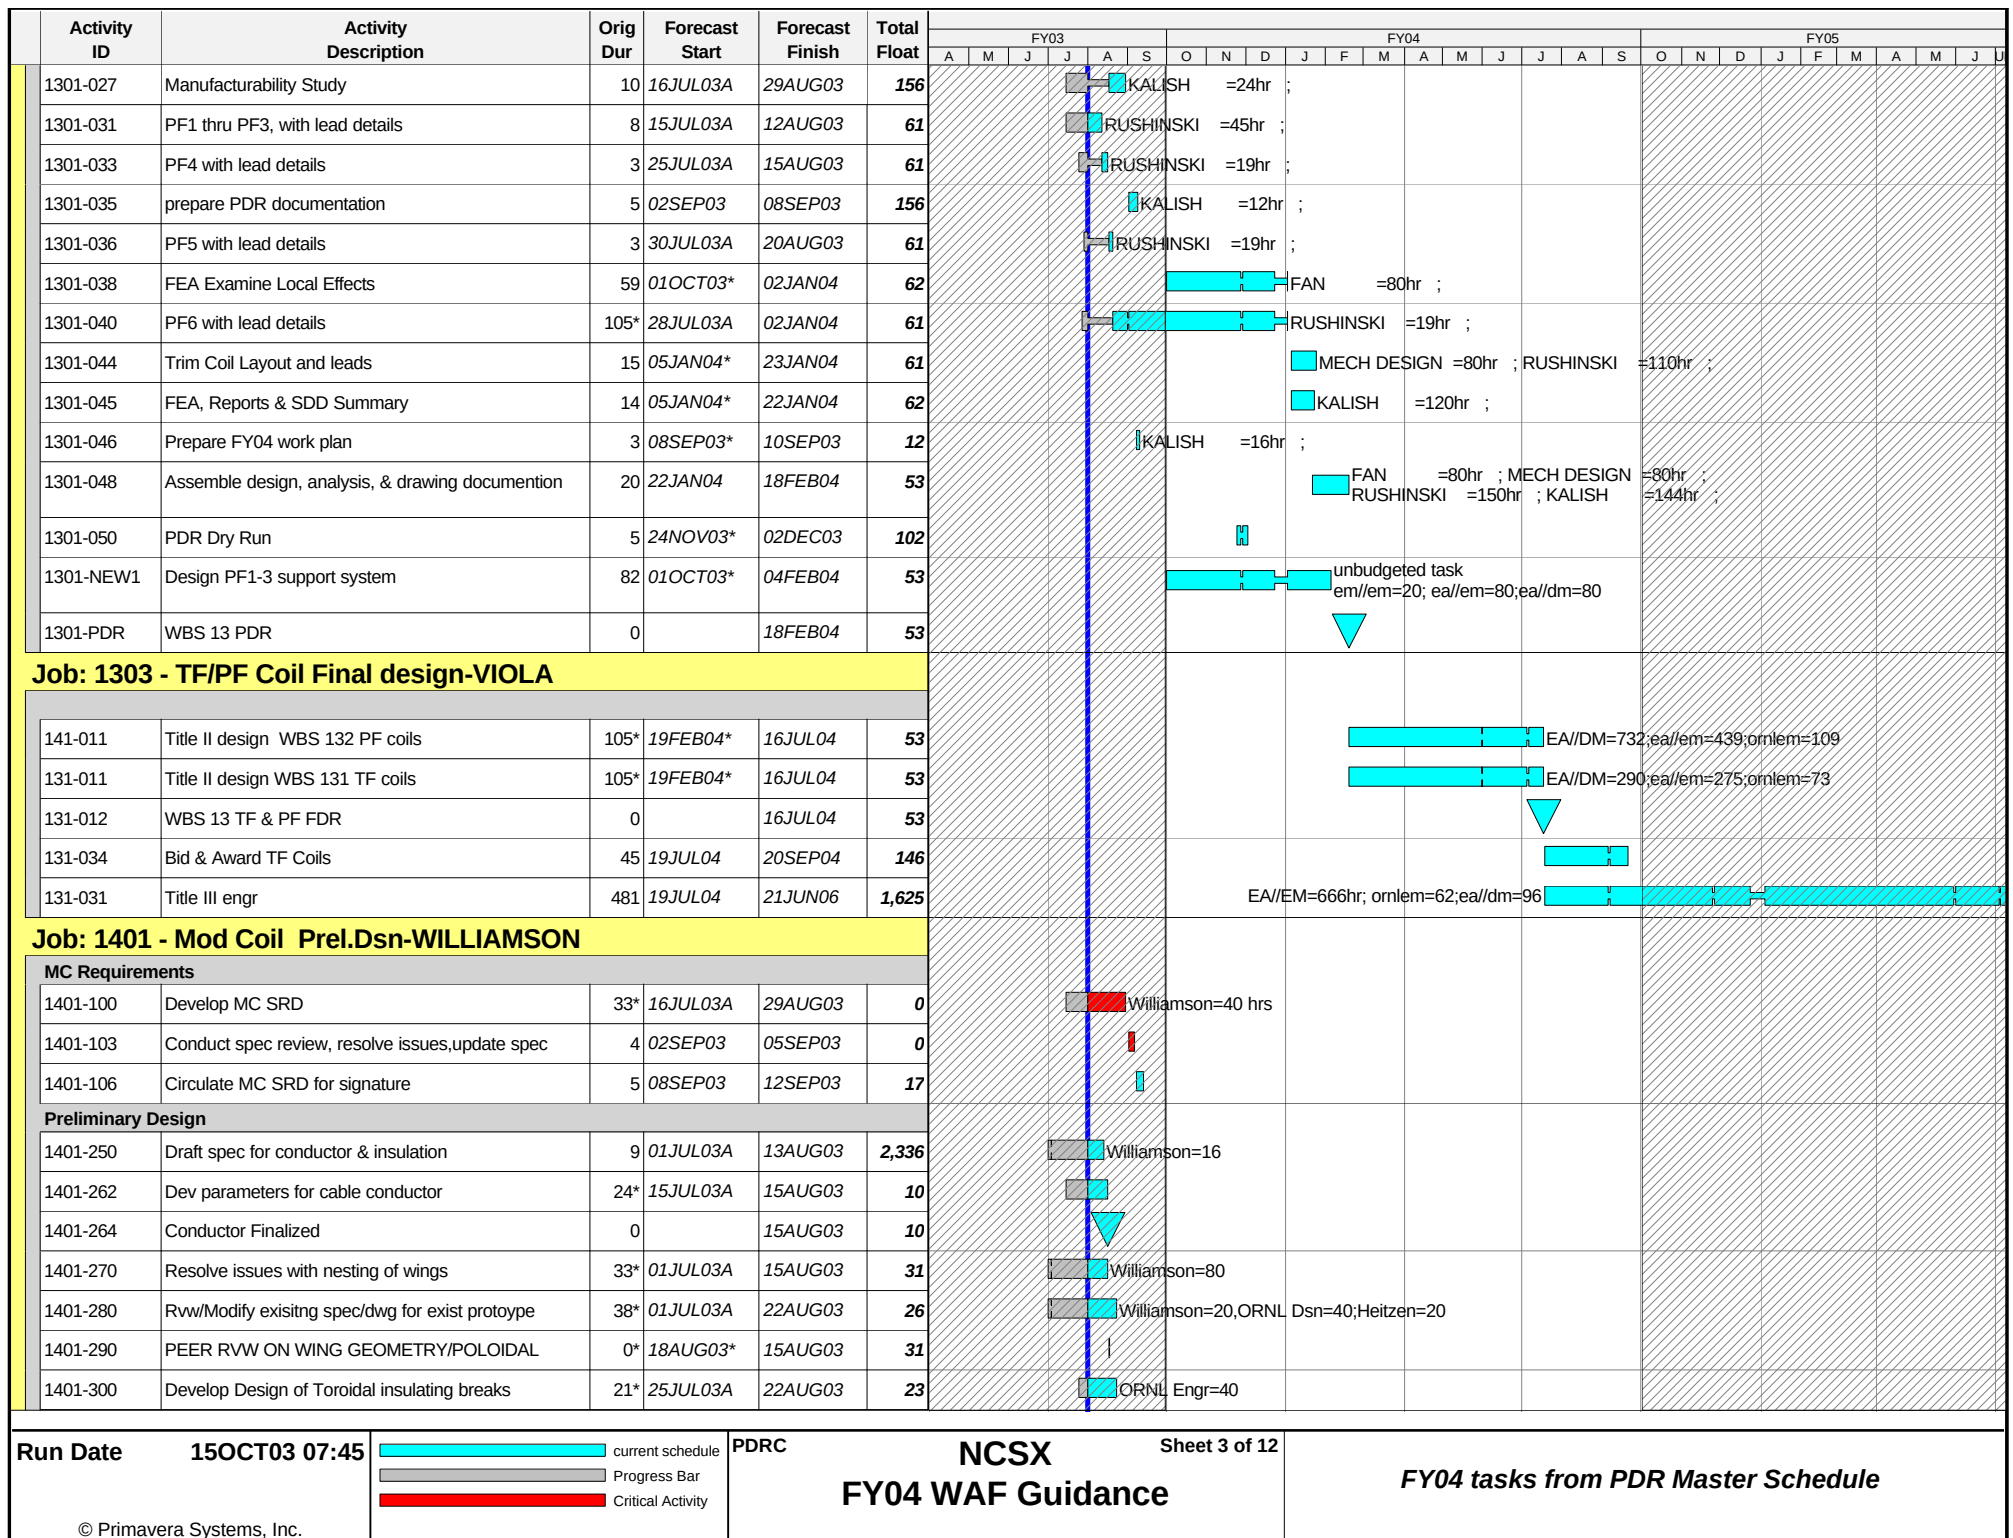

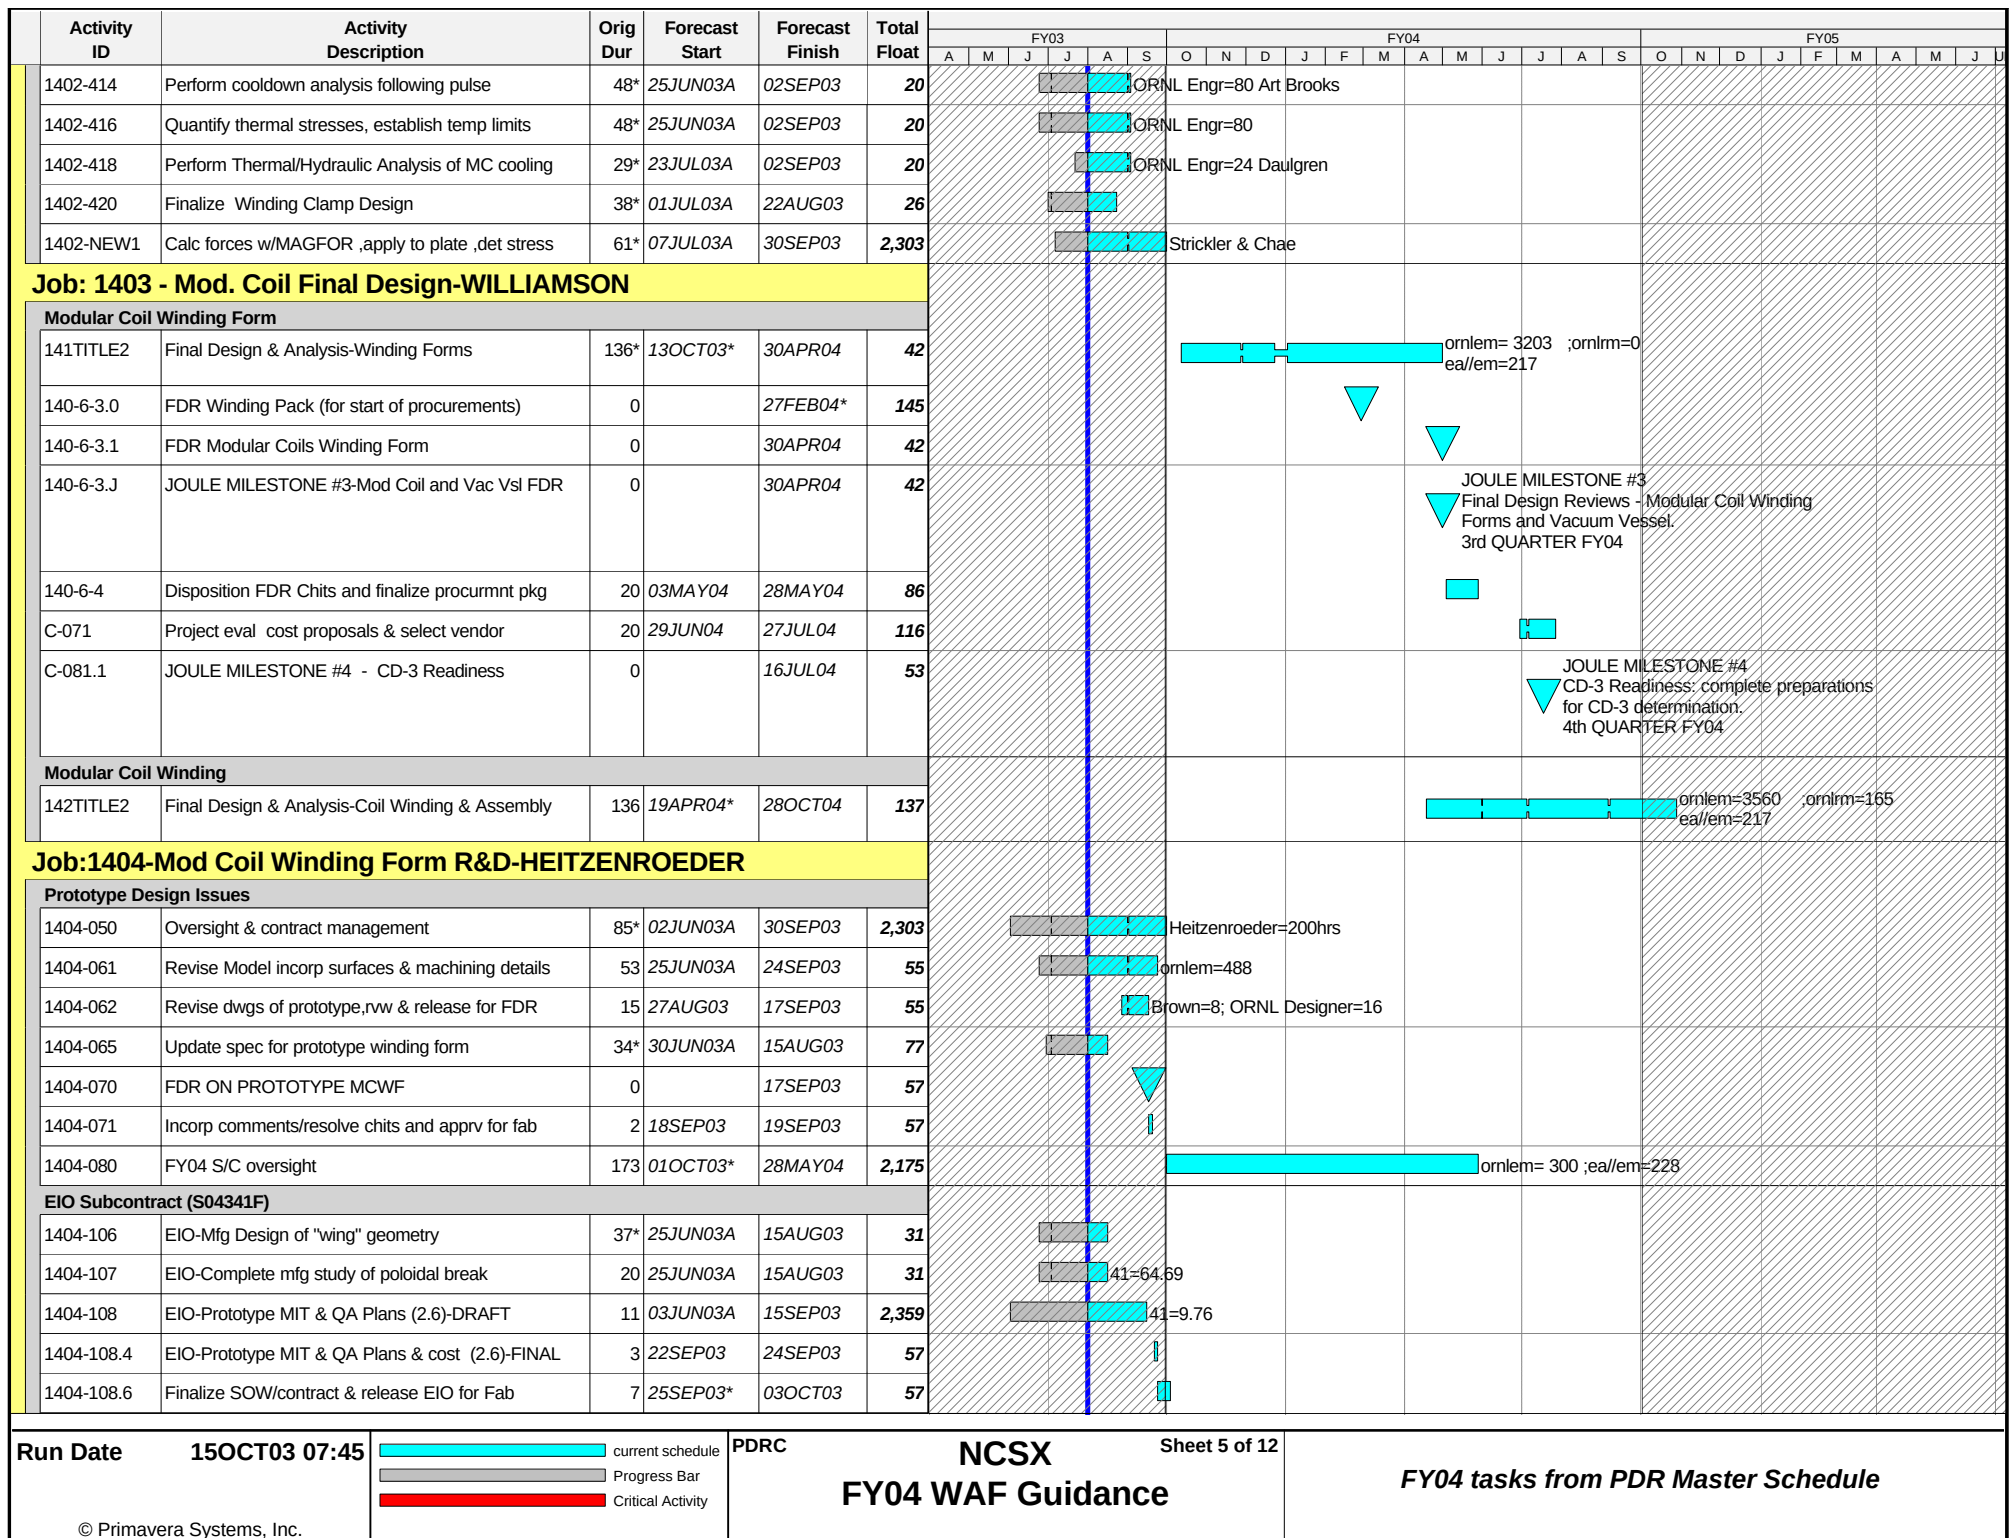

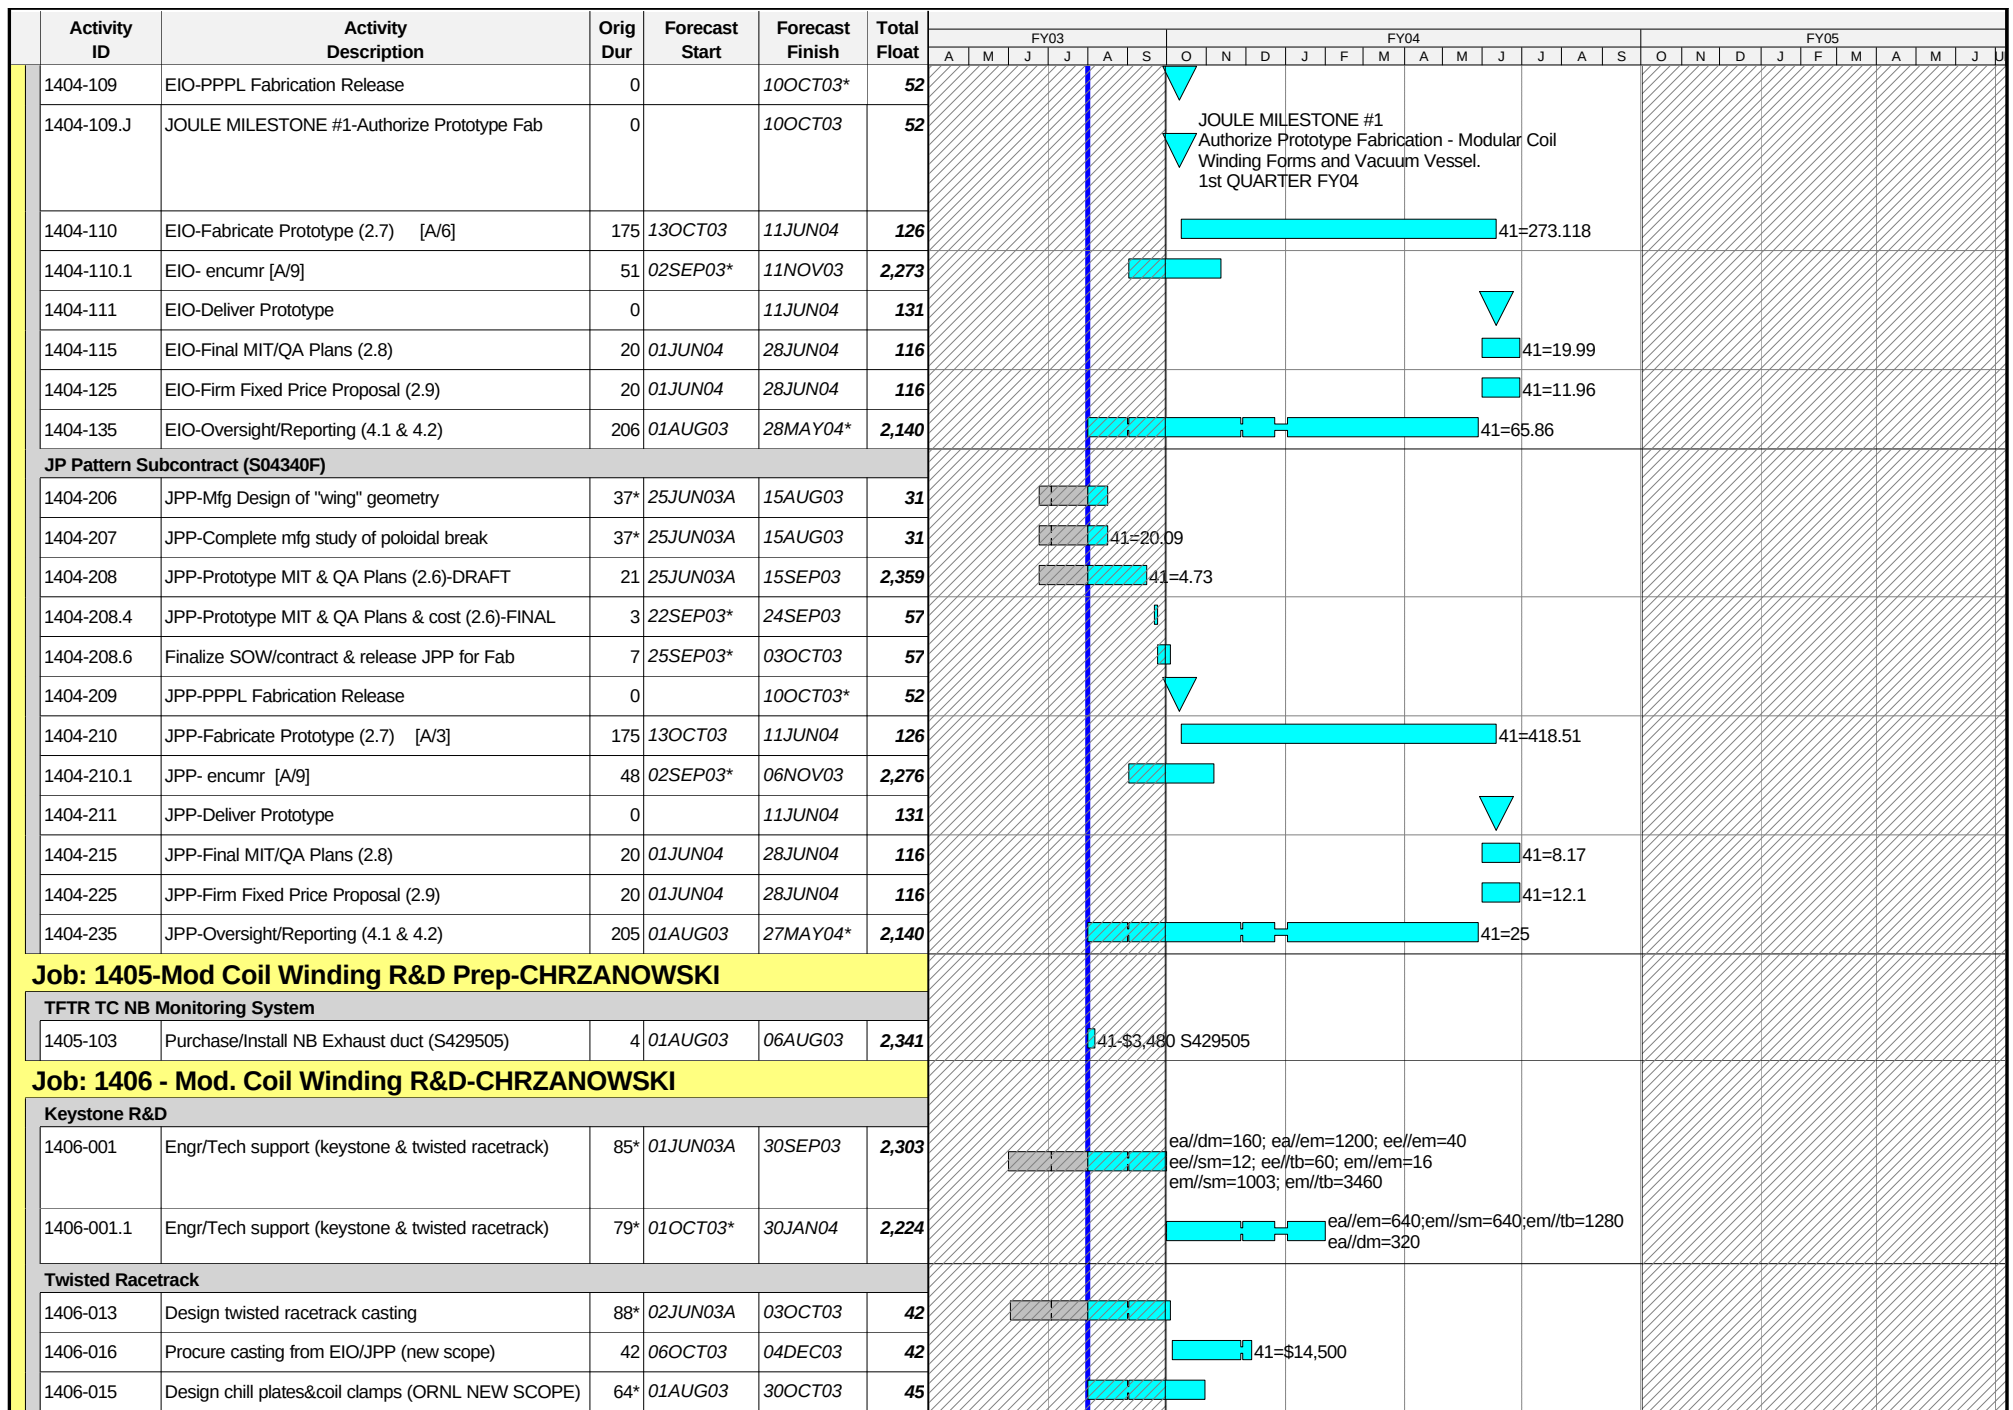

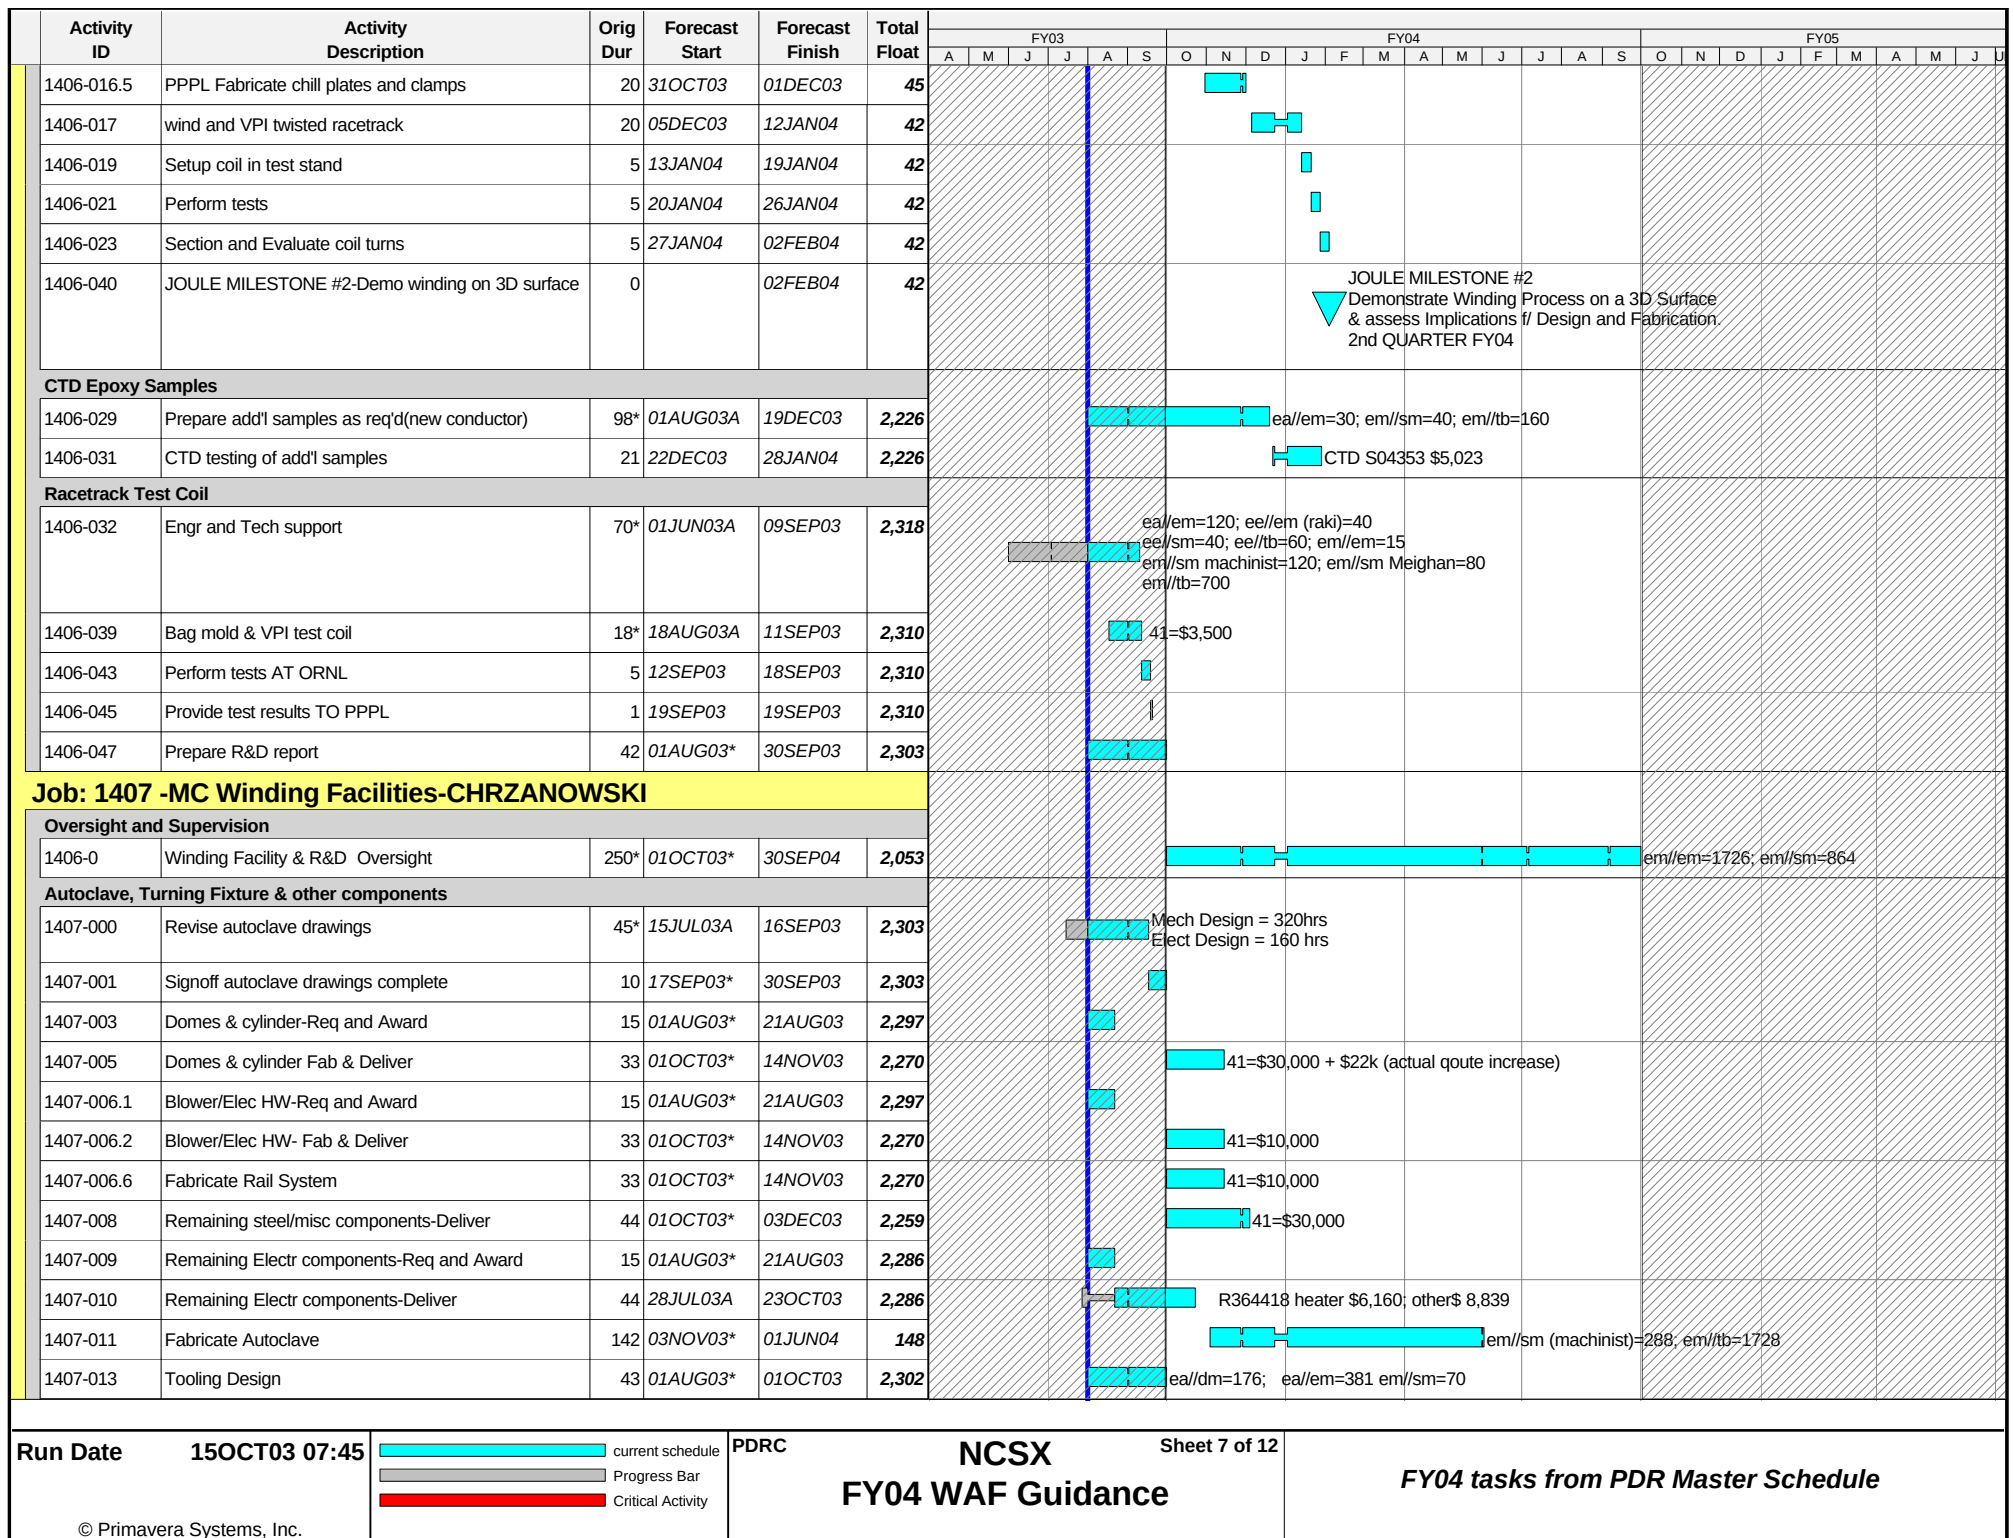

Activity ID	Activity Description	Orig Dur	Forecast Start	Forecast Finish	Total Float	FY03							FY04												FY05																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
						A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
GPP010	Control Room HVAC **GPP**	1	01AUG03	01AUG03	2,344																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
