NCSX Modular Coil Casting R&D / Production Schedule
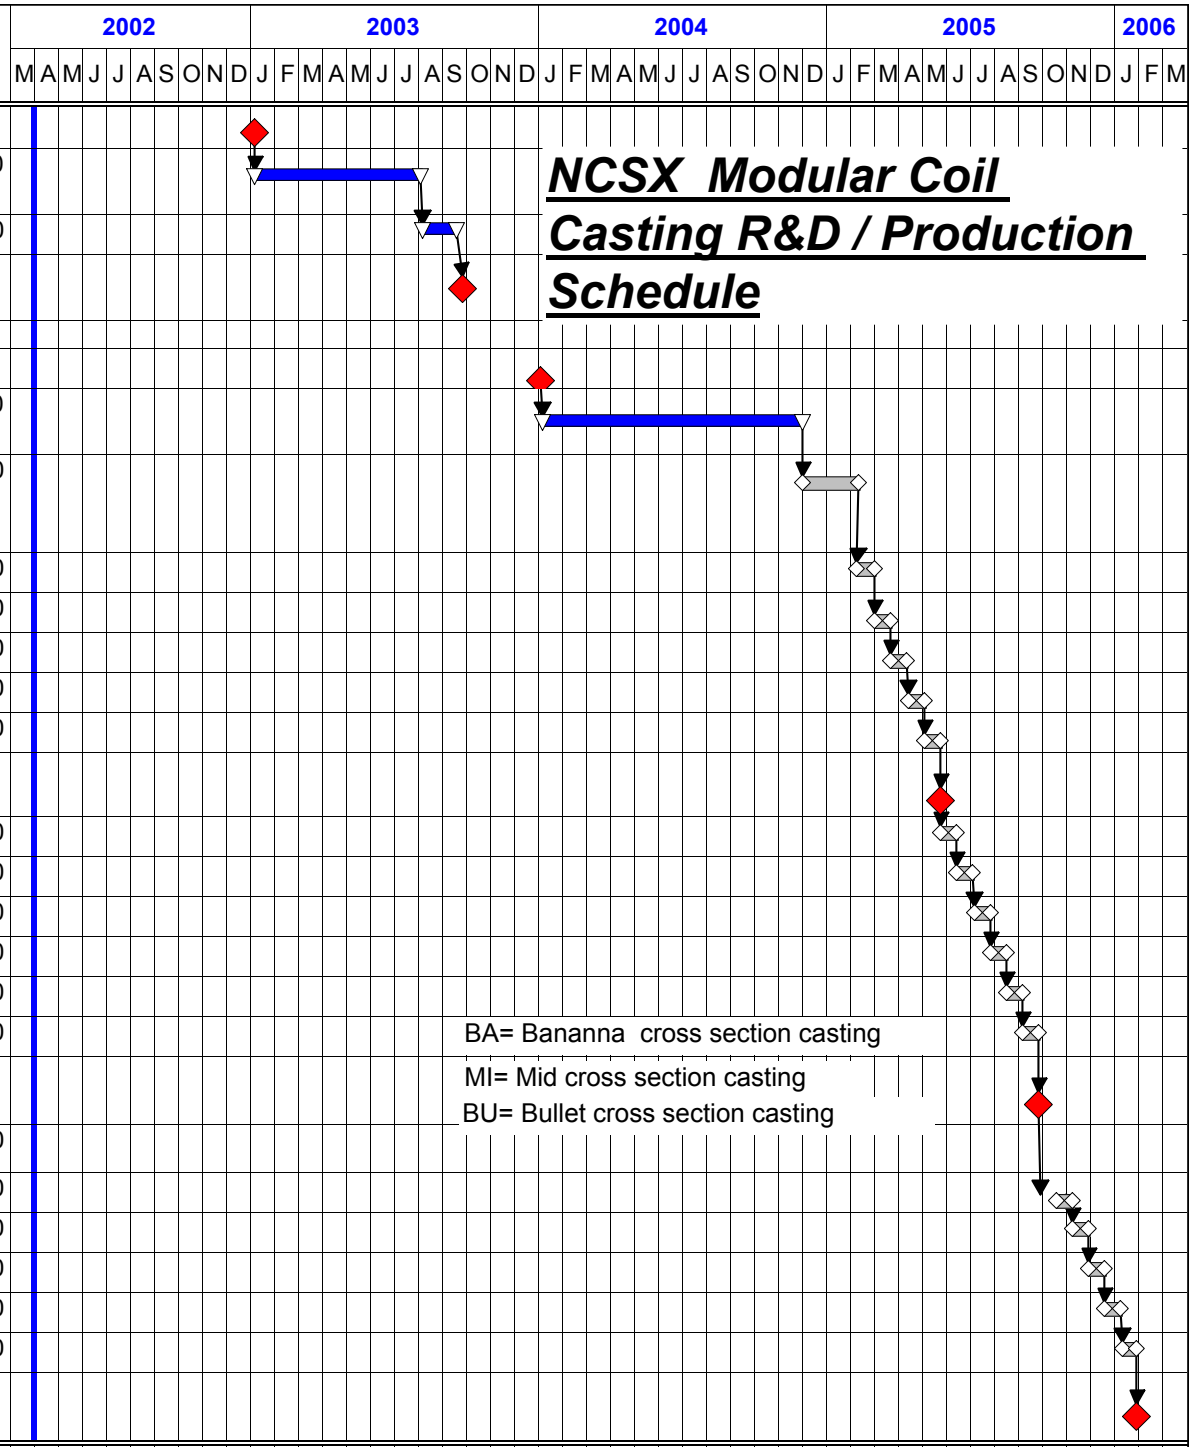
	Activity Name	Start Date	Finish Date	Duration
1	*Contract for R&D Placed*	1/6/03		
2	*R&D casting tooling preparation*	1/7/03	8/4/03	150.00
3	*Produce R&D Casting*	8/5/03	9/19/03	34.00
4	*R&D Casting Received at PPPL*	9/25/03		
5				
6	*Contract for Mfg. Placed*	1/2/04		
7	*Production casting tooling preparation*	1/5/04	11/30/04	237.00
8	*BA-1-1 (Type-Casting #-Field Period #)*	12/1/04	2/9/05	51.00
9	*MI-2-1*	2/8/05	2/28/05	15.00
10	*BU-3-1*	3/1/05	3/21/05	15.00
11	*BA-4-1*	3/22/05	4/11/05	15.00
12	*MI-5-1*	4/12/05	5/2/05	15.00
13	*BU-6-1*	5/3/05	5/23/05	15.00
14	*Milestone: 1st field period castings complete*	5/23/05		
15	*BA-7-2*	5/24/05	6/13/05	15.00
16	*MI-8-2*	6/14/05	7/4/05	15.00
17	*BU-9-2*	7/5/05	7/25/05	15.00
18	*BA-10-2*	7/26/05	8/15/05	15.00
19	*MI-11-2*	8/16/05	9/5/05	15.00
20	*BU-12-2*	9/6/05	9/26/05	15.00
21	*Milestone: 2nd field period castings complete*	9/26/05		
22	*BA-13-3*	9/27/05	10/17/05	15.00
23	*MI-14-3*	10/18/05	11/7/05	15.00
24	*BU-15-3*	11/8/05	11/28/05	15.00
25	*BA-16-3*	11/29/05	12/19/05	15.00
26	*MI-17-3*	12/20/05	1/9/06	15.00
27	*BU-18-3*	1/10/06	1/30/06	15.00
28	*Milestone: 3rd field period castings complete*	1/30/06
