# NCSX REBASELINE PLAN

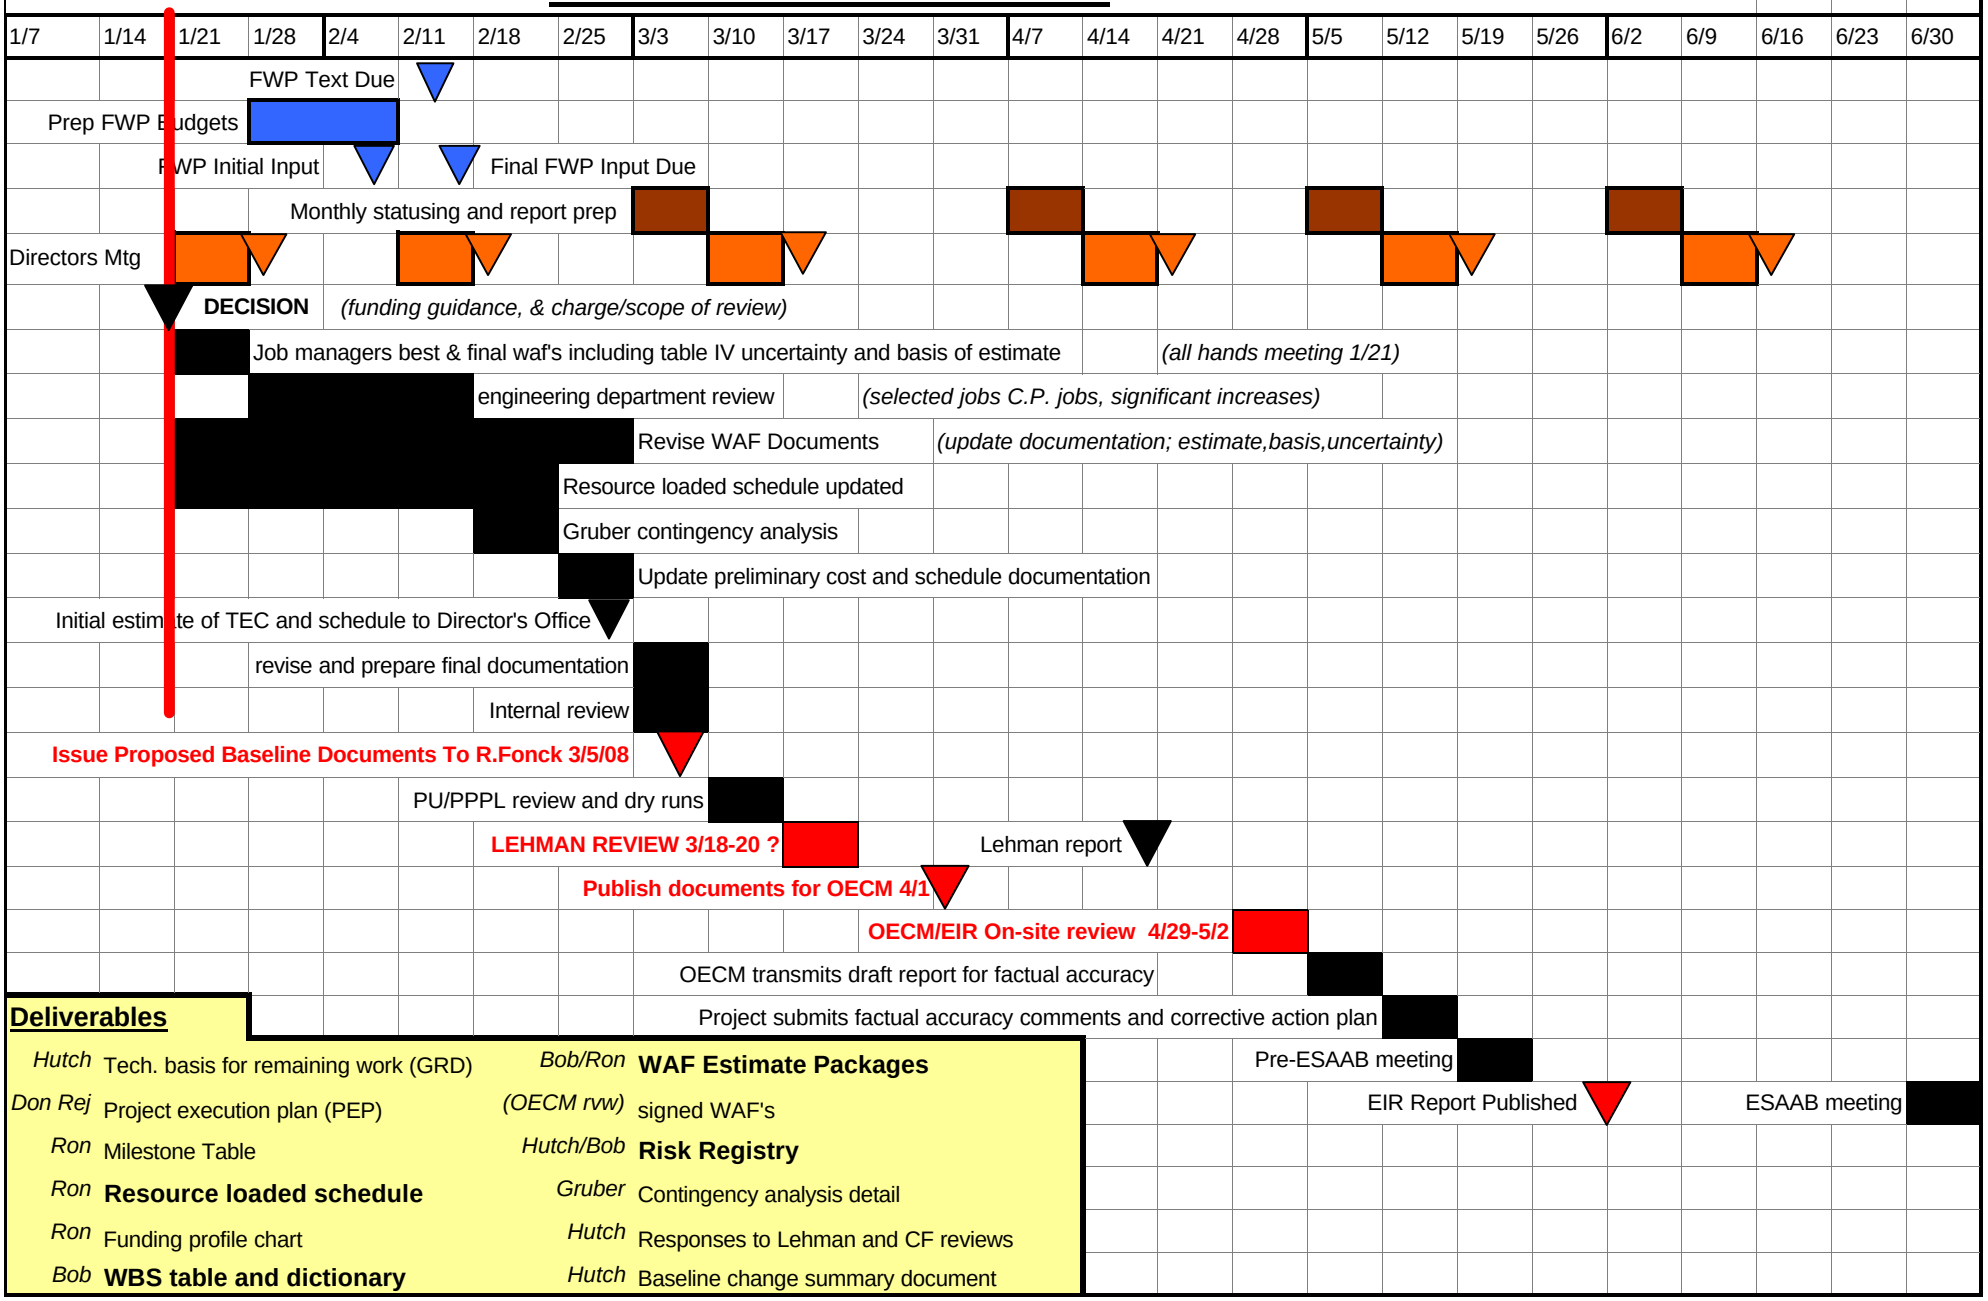


## Deliverables

| | | | |
|---|---|---|---|
| *Hutch* | Tech. basis for remaining work (GRD) | *Bob/Ron* | **WAF Estimate Packages** |
| *Don Rej* | Project execution plan (PEP) | *(OECM rvw)* | signed WAF's |
| *Ron* | Milestone Table | *Hutch/Bob* | **Risk Registry** |
| *Ron* | **Resource loaded schedule** | *Gruber* | Contingency analysis detail |
| *Ron* | Funding profile chart | *Hutch* | Responses to Lehman and CF reviews |
| *Bob* | **WBS table and dictionary** | *Hutch* | Baseline change summary document |
